

Project Update

St. Pius X Catholic School

January 5, 2024



WE BUILD GREAT SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .

Table of Contents



- Team Members
- Summary Report
- Weekly Progress Update
- Subcontractors
- Project Milestones
- Look Ahead Schedule
- Progress Updates
- Project Photos
- Contact Information



PARRISH
CONSTRUCTION GROUP

TEAMS

WE BUILD GREAT

ST. PIUS CATHOLIC SCHOOL TEAM MEMBERS



Owner	Architect/Engineer	Parrish Construction Group
<ul style="list-style-type: none">• Catholic Education of North Georgia, Inc.• St. Pius X Catholic High School	<ul style="list-style-type: none">• CDH Architecture	<ul style="list-style-type: none">• David Loudermilk, Project Director• Alex Johnson, Project Manager• Art Cofelice, Superintendent• Trey DeRieux, Project Engineer• Drew Plunkett, Asst. Superintendent• Zack Cofelice, Asst. Superintendent



PARRISH
CONSTRUCTION GROUP

SUMMARY REPORT

WE BUILD GREAT

SUMMARY REPORT

Month	Calendar Days	Planned Weather Days	Claimed Weather Days
MARCH 2023	31	6	3
APRIL 2023	30	4	4
MAY 2023	31	2	1
JUNE 2023	30	3	2
JULY 2023	31	4	3
AUGUST 2023	31	3	9
SEPTEMBER 2023	30	2	3
OCTOBER 2023	31	3	1
NOVEMBER 2023	30	5	2
DECEMBER 2023	31	8	1
JANUARY 2024	31	11	1
FEBRUARY 2024	29	8	-
MARCH 2024	31	6	-

Critical Tasks	% Complete
SITWORK	90%
FOUNDATIONS	95%
UNDERGROUND UTILITIES	100%
SLAB ON GRADE/DECK	100%
STEEL	95%
ELECTRICAL	85%
PLUMBING	85%
MECHANICAL	85%
ROOFING	90%



PARISH
CONSTRUCTION GROUP

PROGRESS UPDATE

WE BUILD GREAT _____.

WEEKLY PROGRESS UPDATE

- SWITCHBACK RAMPS CONTINUED
- INSTALLING INTERIOR STOREFRONT FRAMES AND WINDOWS NEXT WEEK
- 1ST COAT OF PAINT CONTINUED
- RETAINING WALL BRICK TO FINISH NEXT WEEK



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Site Work		
GRADING AND UTILITIES	RUBY-COLLINS	95%
UNDERGROUND GAS LINE	POLK COUNTY PUBLIC SERVICE	100%
Building Systems		
MECHANICAL	GEORGIA MECHANICAL	85%
ELECTRICAL	ALL STATE ELECTRICAL CONTRACTORS	85%
PLUMBING	POLK COUNTY PUBLIC SERVICE	85%
FIRE PROTECTION	GAINESVILLE FIRE PROTECTION	90%
Building Structure		
FOUNDATION AND SLAB ON GRADE (SOG)/DECK	PARRISH CONCRETE	100%
STRUCTURAL STEEL FRAMING	TRINITY FABRICATORS	95%
EXTERIOR WALLS	PARRISH MASONRY	100%
INTERIOR WALLS	PARRISH MASONRY/HOLT & HOLT	100%



PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE

WE BUILD GREAT

SUBCONTRACTOR PROGRESS

Scope of Work	Subcontractor	Percent Complete
Building Envelope		
BRICK	PARRISH MASONRY	95%
WINDOWS/STOREFRONT	COMMERCIAL GLASS & MIRRORS	80%
Building Interiors		
FLOORING	PERIMETER FLOORS	0%
DRYWALL	HOLT & HOLT	90%
CEILINGS	HOLT & HOLT	75%
PAINTING	MCs PAINTING	60%




PARRISH
CONSTRUCTION GROUP

PROJECT UPDATE


WE BUILD GREAT

PROGRESS UPDATE

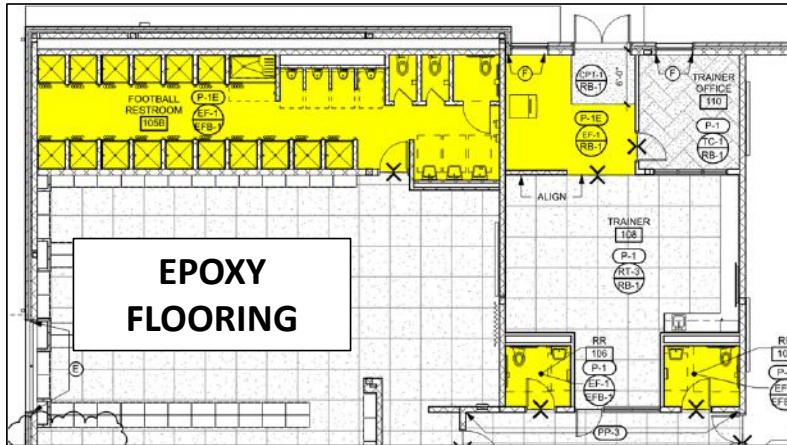

**GREEN HIGHLIGHTED SECTIONS
HAVE BEEN COMPLETED; YELLOW
HIGHLIGHTED IN PROGRESS**

**SWITCHBACK RAMP WALLS
POURED; EPOXY FLOORING IN
PROGRESS; OVERHEAD MEPs
FINISHING UP**

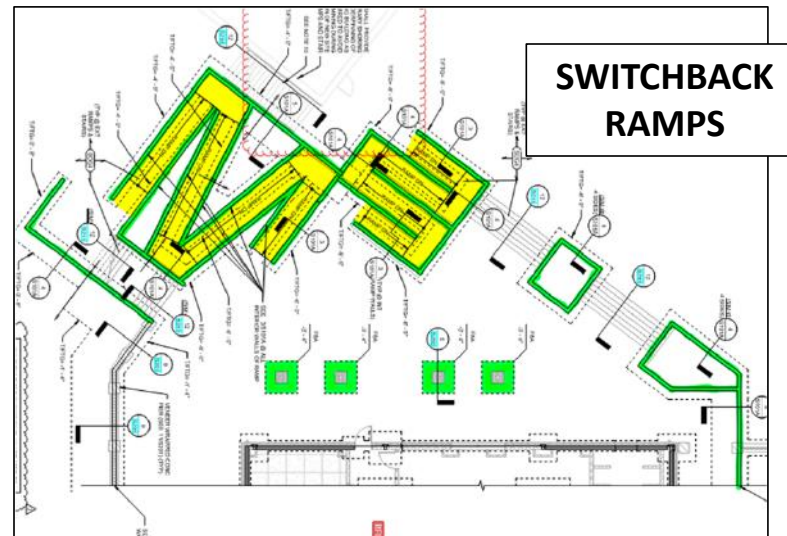

**INTERIOR STOREFRONT IN
PROGRESS NEXT WEEK; SITE
CONCRETE AND RAMPS IN
PROGRESS NEXT WEEK; EPOXY
FLOORING CONTINUED; DRYFALL
PAINT IN WEIGHT ROOM TO BE
INSTALLED NEXT WEEK**



PARISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



**SWITCHBACK RAMP FOUNDATIONS AND
WALLS Poured**



PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS

FRONT PARKING LOT





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT

PROJECT PHOTOS

**BACKFILLING SWITCHBACKS GETTING
READY TO POUR RAMPS**





PARRISH
CONSTRUCTION GROUP

PROJECT PHOTOS

WE BUILD GREAT _____.

PROJECT PHOTOS



PREPPING FOR EPOXY FLOORING

Contact Information



David Loudermilk

Project Director
478.256.1839

dloudermilk@parrishconstruction.com



Alex Johnson

Project Manager
470.540.0047

ajohnson@parrishconstruction.com



Art Cofelice

Sr. Superintendent
770.880.3762

acofelice@parrishconstruction.com



Zack Cofelice

Superintendent
470.925.3525

zcofelice@parrishconstruction.com



Trey DeRieux

Project Engineer
470.442.3169

tderieux@parrishconstruction.com



Drew Plunkett

Asst. Superintendent
678.215.5193

dplunkett@parrishconstruction.com

WE BUILD GREAT SCHOOLS INDUSTRIAL FACILITIES HEALTHCARE FACILITIES COMMUNITIES LEADERS FUTURES .
